
| ID |      | Outline Task Name                                      | Duration | Start        | Finish       | NA L   | 1.      |          | ر ا   | 0   N   D        | 2022       | - L        | M A M J J                    |           | ر ا     | 0   N         | 20       | 023      | 10        | A   NA   | 1.1       |         | ,   c           |         | N D          | 2024          | 14   4     | N   N4  |
|----|------|--------------------------------------------------------|----------|--------------|--------------|--------|---------|----------|-------|------------------|------------|------------|------------------------------|-----------|---------|---------------|----------|----------|-----------|----------|-----------|---------|-----------------|---------|--------------|---------------|------------|---------|
| 0  | Mode |                                                        | 488 days | Thu 5/6/21   | Fri 8/25/23  | IVI J  | J       | A        | 5     | O N D            | J          | F N        | M A M J J                    | A         | 5       | UN            | D        | J F      | IVI       | A IVI    | J         | J /     | 4 5             | 0       | N D          | J F           | IVI P      | · IVI   |
| 1  | -5   | 1 Project Milestones                                   | 584 days | Thu 5/6/21   | Fri 8/25/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           |         | <b>-</b>        |         |              |               |            |         |
| 2  | -5   | 2 Design Milestones                                    | 192 days | Thu 5/6/21   | Wed 2/9/22   |        |         |          |       |                  |            | 1          |                              |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 3  | -5   | Notice to Proceed (Design)                             | 0 days   | Thu 5/6/21   | Thu 5/6/21   | Notice | to Proc | eed (Des | sign) |                  |            |            |                              |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 4  | -5   | 3 Schematic Design (SD) Complete                       | 0 days   | Thu 7/1/21   | Thu 7/1/21   | 7/1    | ♦ Sch   | ematic [ | Desig | n (SD) Complete  |            |            |                              |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 5  | -5   | 3 Design Development (DD) Complete                     | 0 days   | Fri 10/1/21  | Fri 10/1/21  |        |         | 10,      | /1 🌢  | Design Develop   | ment (D    | D) Cor     | mplete                       |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 6  | -5   | 3 CP1 - Permit Set (Site/Utility/Foundation/Structure) | 0 days   | Fri 10/29/21 | Fri 10/29/21 |        |         |          | 10/   | /29 🔷 CP1 - Perr | nit Set (S | Site/Ut    | tility/Foundation/Structure  | e)        |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 7  | -5   | 3 Construction Documents (CD) Complete                 | 0 days   | Wed 1/26/22  | Wed 1/26/22  |        |         |          |       | 1                | /26 🄷 (    | Constru    | uction Documents (CD) Cor    | mplete    |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 8  | -5   | CP2 - Permit Set (Office Building & Finishes)          | 0 days   | Wed 2/9/22   | Wed 2/9/22   |        |         |          |       |                  | 2/9        | CP2        | - Permit Set (Office Buildin | ng & Fini | shes)   |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 9  | -5   | CP3 - Permit Set (Multi-Family Building & Finishes)    | 0 days   | Wed 2/9/22   | Wed 2/9/22   |        |         |          |       |                  | 2/9        | <b>СРЗ</b> | - Permit Set (Multi-Family   | Building  | g & Fin | ishes)        |          |          |           |          |           |         |                 |         |              |               |            |         |
| 10 | -5   | 2 Construction Milestones                              | 419 days | Tue 1/4/22   | Fri 8/25/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           |         | -               |         |              |               |            |         |
| 11 | -5   | 3 Mobilize                                             | 0 days   | Tue 1/4/22   | Tue 1/4/22   |        |         |          |       | 1/4              | Mobi       | ilize      |                              |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 12 | -5   | 3 Site Demo & Utilities Start                          | 0 days   | Tue 1/4/22   | Tue 1/4/22   |        |         |          |       | 1/4              | Site D     | Demo 8     | & Utilities Start            |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 13 | -5   | 3 Foundations Start                                    | 0 days   | Mon 2/28/22  | Mon 2/28/22  |        |         |          |       |                  | 2/2        | 28 ♦ F     | Foundations Start            |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 14 | -5   | 3 Parking Structure Start                              | 0 days   | Mon 5/16/22  | Mon 5/16/22  |        |         |          |       |                  |            |            | 5/16 🄷 Parking Stru          | icture St | art     |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 15 | -5   | 3 Multi-Family Structure Start                         | 0 days   | Thu 9/15/22  | Thu 9/15/22  |        |         |          |       |                  |            |            |                              | 9/15      | ♠ M     | ulti-Family S | tructur  | e Start  |           |          |           |         |                 |         |              |               |            |         |
| 16 | -5   | 3 Office Structure Start                               | 0 days   | Wed 9/28/22  | Wed 9/28/22  |        |         |          |       |                  |            |            |                              | 9/        | 28 🄷    | Office Struc  | ture St  | art      |           |          |           |         |                 |         |              |               |            |         |
| 17 | -5   | Parking Structure Complete                             | 0 days   | Thu 10/27/22 | Thu 10/27/22 |        |         |          |       |                  |            |            |                              |           | 10/     | 27 🄷 Parkir   | ng Struc | ture Co  | plete     |          |           |         |                 |         |              |               |            |         |
| 18 | -5   | 3 Office Structure Complete                            | 0 days   | Thu 1/5/23   | Thu 1/5/23   |        |         |          |       |                  |            |            |                              |           |         |               | 1/5 🔷    | Office S | ructure   | Comple   | te        |         |                 |         |              |               |            |         |
| 19 | -5   | 3 Multi-Family Structure Complete                      | 0 days   | Thu 1/19/23  | Thu 1/19/23  |        |         |          |       |                  |            |            |                              |           |         |               | 1/19     | Mult     | -Family : | Structur | e Comple  | te      |                 |         |              |               |            |         |
| 20 | -5   | Office Building Substantially Complete / TCO           | 0 days   | Fri 7/14/23  | Fri 7/14/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          | 7/14      | Offi    | e Buildir       | g Subst | antially Co  | omplete / 1   | гсо        |         |
| 21 | -5   | Multi-Family Building Substantially Complete / TCO     | 0 days   | Tue 8/22/23  | Tue 8/22/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           | 8/22    | Multi           | Family  | Building S   | Substantial   | y Complet  | ₂ / TCO |
| 22 | -5   | 3 ALL Buildings - FINAL Certificate of Occupancy       | 0 days   | Fri 8/25/23  | Fri 8/25/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           | 8/25    | ALL E           | uilding | s - FINAL C  | Certificate o | of Occupan | су      |
| 23 | -5   | 3 Construction Summary Bars                            | 345 days | Tue 1/4/22   | Wed 8/23/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           |         | <b>-1</b>       |         |              |               |            |         |
| 24 | -5   | 4 Enabling Sitework & Demolition                       | 27 days  | Tue 1/4/22   | Fri 2/25/22  |        |         |          |       |                  |            | E          | nabling Sitework & Demol     | lition    |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |
| 25 | -    | 4 Foundation Systems - ALL                             | 52 days  | Mon 2/28/22  | Tue 5/24/22  |        |         |          |       |                  |            | -          | Foundation                   | n Systei  | ns - Al | LL            |          |          |           |          |           |         |                 |         |              |               |            |         |
| 26 | -5   | 4 Parking Garage Construction                          | 205 days | Mon 5/16/22  | Thu 5/4/23   |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           | P        | arking Ga | rage Co | nstructio       | n       |              |               |            |         |
| 27 | -    | 4 Multi-Family Construction                            | 198 days | Thu 9/15/22  | Tue 8/22/23  |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           |         | <b>—</b> Multi- | amily ( | Construction | øn            |            |         |
| 28 | -5   | 4 Office Building Construction                         | 166 days | Wed 9/28/22  | Fri 7/14/23  |        |         |          |       |                  |            |            |                              |           | +       |               |          |          |           |          |           | Offi    | e Buildir       | g Const | truction     |               |            |         |
|    |      |                                                        | I.       |              |              |        |         |          |       |                  |            |            |                              |           |         |               |          |          |           |          |           |         |                 |         |              |               |            |         |





| ID Task<br>Mode | Outline Task Name                                    | Duration   | Start        | Finish       | N4   1   1 | A   C | 0   N | 2022 | <br>N4   A   N4   I   I |                                | 2023<br>J F M A M J J A S                           | 2024                                   |
|-----------------|------------------------------------------------------|------------|--------------|--------------|------------|-------|-------|------|-------------------------|--------------------------------|-----------------------------------------------------|----------------------------------------|
| 144             |                                                      | 25 days    | Mon 2/28/22  | Thu 4/7/22   | IVI J J    | A 3   | U     | D J  |                         | stems - Drilled Piers (118ea @ |                                                     |                                        |
| 147             | 3 Shallow Foundation Systems                         | 35 days    | Mon 3/28/22  | Tue 5/24/22  |            |       |       |      | Shallow Fo              | undation Systems               |                                                     |                                        |
| 151             | 2 Cast-in-Place Concrete Structures                  | 144 days   | Mon 5/16/22  | Thu 1/19/23  |            |       |       |      | <u> </u>                |                                | Cast-in-Place Concrete Structures                   |                                        |
| 152             | Parking Garage - 500 stall & Retail CIP (226,000-sf) | 100 days   | Mon 5/16/22  | Thu 10/27/22 |            |       |       |      |                         | Parking G                      | rage - 500 stall & Retail CIP (226,000-sf)          |                                        |
| 153             | Parking Garage - North (Multi-Family) - 142,000-st   | f 100 days | Mon 5/16/22  | Thu 10/27/22 |            |       |       |      |                         | Parking G                      | rage - North (Multi-Family) - 142,000-sf            |                                        |
| 163             | Parking Garage - South (Office) 84,000-sf            | 80 days    | Mon 5/16/22  | Tue 9/27/22  |            |       |       |      |                         | Parking Garage                 | South (Office) 84,000-sf                            |                                        |
| 173             | Multi-Family Building CIP - Levels 5-10 (138,200-sf) | 72 days    | Thu 9/15/22  | Thu 1/19/23  |            |       |       |      |                         | -                              | Multi-Family Building CIP - Levels 5-10 (138,200-sf |                                        |
| 186             | Office Building CIP - Levels 5-9 (102,300-sf)        | 58 days    | Wed 9/28/22  | Thu 1/5/23   |            |       |       |      |                         |                                | Office Building CIP - Levels 5-9 (102,300-sf)       |                                        |
| 198             | 2 Enclosure - Exterior Skin Systems & Roofing        | 152 days   | Wed 9/28/22  | Thu 6/22/23  |            |       |       |      |                         |                                | Enclosure - Exterior                                | Skin Systems & Roofing                 |
| 199             | Parking Garage / Retail Envelope                     | 94 days    | Wed 9/28/22  | Thu 3/16/23  |            |       |       |      |                         |                                | Parking Garage / Retail Envelope                    |                                        |
| 214             | 3 Office Envelope                                    | 90 days    | Tue 11/1/22  | Thu 4/13/23  |            |       |       |      |                         |                                | Office Envelope                                     |                                        |
| 237             | 3 Multi-Family Envelope                              | 124 days   | Thu 11/10/22 | Thu 6/22/23  |            |       |       |      |                         | _                              | Multi-Family Envelo                                 | pe                                     |
| 273             | 2 MEP Systems & Equipment Rough-In/Install           | 156 days   | Fri 10/28/22 | Mon 6/12/23  |            |       |       |      |                         |                                | MEP Systems & Equip                                 | ment Rough-In/Install                  |
| 284             | 2 Finishes                                           | 161 days   | Fri 1/6/23   | Tue 8/22/23  |            |       |       |      |                         |                                | Finishe                                             |                                        |
| 285             | 3 Parking Garage/Retail - Interior & Finishes        | 51 days    | Mon 1/30/23  | Tue 4/25/23  |            |       |       |      |                         |                                | Parking Garage/Retail - Interior                    |                                        |
| 290             | 3 Office Building - Tenant Interiors & Finishes      | 134 days   | Fri 1/6/23   | Fri 7/14/23  |            |       |       |      |                         |                                |                                                     | Tenant Interiors & Finishes            |
| 301             |                                                      |            | Fri 1/20/23  | Tue 8/22/23  |            |       |       |      |                         |                                |                                                     | mily - Interior & Finishes             |
| 308             |                                                      |            |              | Fri 8/25/23  |            |       |       |      |                         |                                |                                                     | ut, Start-Up, Inspections              |
| 309             |                                                      | 43 days    | Thu 3/2/23   | Mon 5/1/23   |            |       |       |      |                         |                                | Equipment Start-Up                                  |                                        |
| 314             |                                                      | 98 days    |              |              |            |       |       |      |                         |                                | Punch L                                             |                                        |
| 318             |                                                      | 86 days    | Wed 4/26/23  |              |            |       |       |      |                         |                                |                                                     | sioning & Inspections                  |
| 319             |                                                      | 42 days    | Fri 6/16/23  | Tue 8/22/23  |            |       |       |      |                         |                                | Commis                                              |                                        |
| 322             |                                                      | 73 days    | Wed 4/26/23  |              |            |       |       |      |                         |                                |                                                     | pections & Final Life Safety           |
| 323             | 4 Life Safety Inspections - Parking Garage           | 5 days     | Wed 4/26/23  | Tue 5/2/23   |            |       |       |      |                         |                                | - Life Safety Inspections - Parkin                  |                                        |
| 324             |                                                      | 5 days     | Mon 7/10/23  |              |            |       |       |      |                         |                                |                                                     | ctions - Office Building/TCO           |
| 325             |                                                      | 5 days     | Wed 8/16/23  |              |            |       |       |      |                         |                                |                                                     | y Inspections - Multi-Family/TCO       |
| 326             |                                                      | 3 days     | Wed 8/23/23  |              |            |       |       |      |                         |                                | Final Ins                                           | pections & Sign-off / Project Complete |
| 327             | 1 Weather Days                                       | 447 days   | Thu 5/6/21   | Wed 6/21/23  |            |       |       |      |                         |                                |                                                     |                                        |
|                 |                                                      |            |              |              |            |       |       |      |                         |                                |                                                     |                                        |

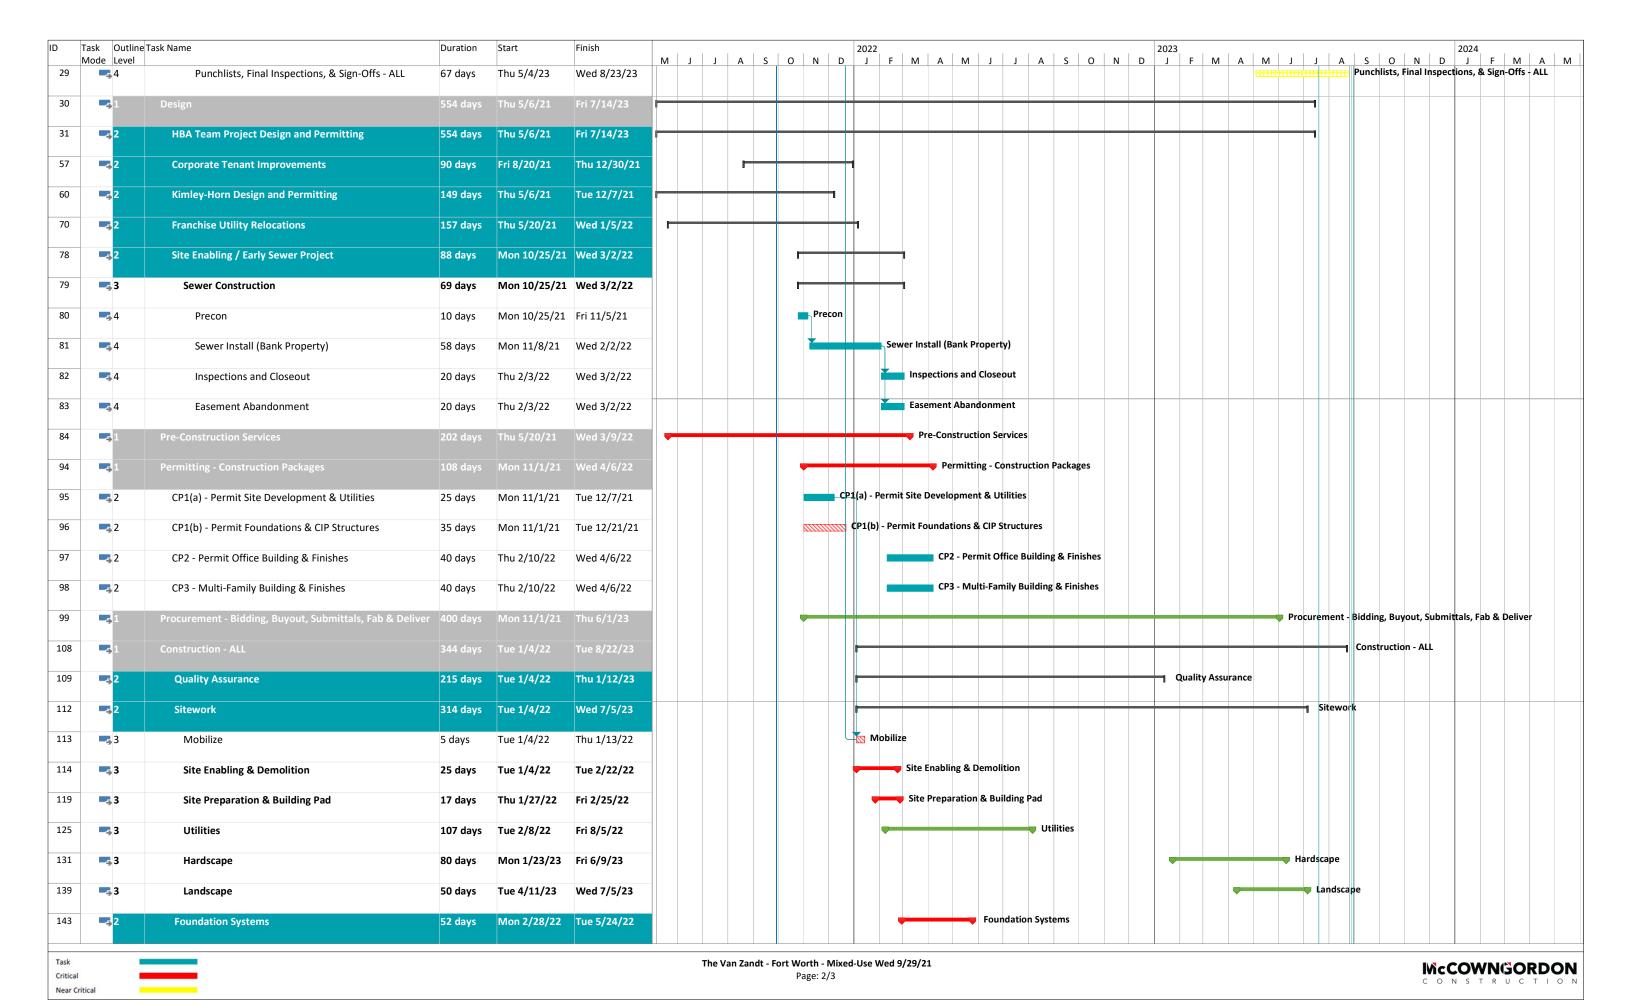
